BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Project Division
Project Name	:	Improvements, Restoration to roads and drains at Dasarahalli, Saraipalya and Rachenahalli surrounding areas in ward no.06
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	01-07-22
Project End Date	:	07-04-23
Project Length in Months	:	09 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Removing and refixing stone slabs of drains and pointing in CM (1:3) (P.No-27,I No-5.33,KPWD SR 2018-19)	Sqm	3156.62	3156.62	100	01-07-22	11-07-22	10
2	KSRRB 300-1. Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications(I No-19.1,	Cum	8669.62	8669.62	100	04-07-22	19-07-22	15
3	Providing granite slabs of selected quality roughly dressed and fixed in cement mortar (1:6) including fixing curing etc., complete. (P.No-27,I No-5.31.1, KPWD SR 2018-19), 7.5cms thick	Cum	2104.04	2104.04	100	14-07-22	24-07-22	10
4	KSRB 4-1.2 : Providing and laying in position plain cement concrete of Mix 1:3:6 with OPC @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0.892cum and fine aggregates @ 0.465cum machine mixed, machine mixed, concrete	Cum	569.49	569.49	100	24-07-22	13-08-22	20
5	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. with 20mm and down size granite metal coarse aggregates at 0.69 cum and fine aggregates at 0.43 cum machine mixed, well	tonne	1187.59	1187.59	100	08-08-22	07-09-22	30
6	KSRRB M2200-6. Providing T.M.T. steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in position, lapping and/or welding wherever required, tying with binding wire and anchoring to the adjoining members	Cum	76.42	76.42	100	23-08-22	27-09-22	35
7	Providing and Fixing pre cast covering Slab 100mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading,	Sqm	2749.23	2749.23	100	12-09-22	22-10-22	40
8	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading,	Sqm	400.11	400.11	100	12-09-22	22-10-22	40
9	KSRRB M300-14. Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and	Sqm	10972.59	10972.59	100	02-07-22	31-08-22	60
10	KSRRB 300-46. Scarifying by mechanical means stone metal crust 50mm to 100mm thick by along with 20mm premix carpet / surface dressing and stacking of old serviceable materials including cost of all labour charges, HOM complete as per specifications.(P.No-146,I No-19.52)	Cum	49184.42	49184.42	100	07-07-22	11-08-22	35
11	Providing, laying, spreading and compacting Stone dust / Grit 4.75 mm to 0.075 mm specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers. (P.No-	M	6026.56	6026.56	100	14-07-22	13-08-22	30

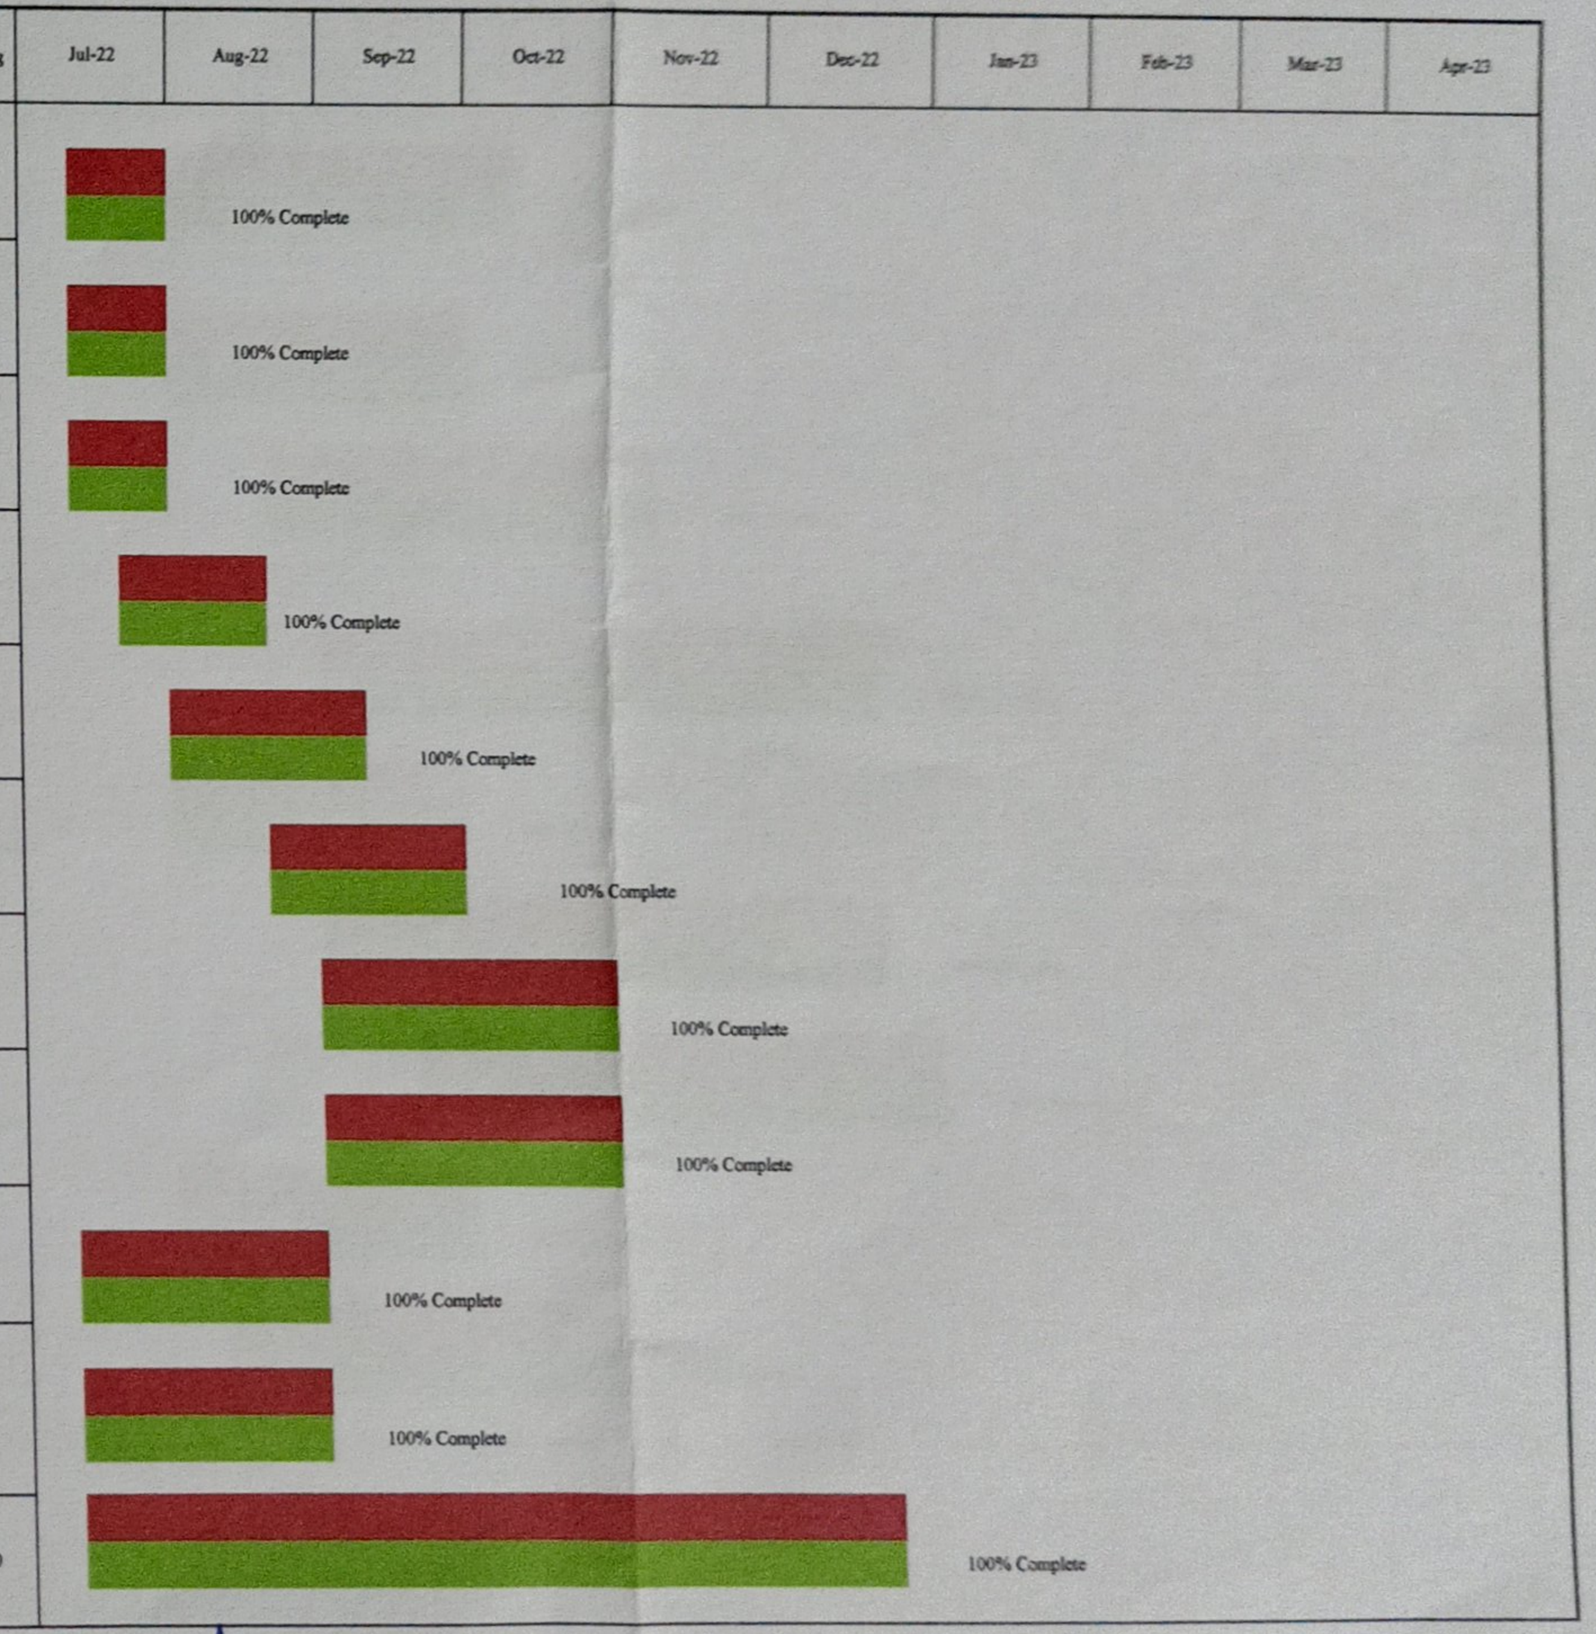

Asst. Executive Engineer
Project Division
Yelahanka Zone
Bangalore - 92

Scanned by TapScanner

Clients Name	:	**BRUHAT BENGALURU MAHANAGARA PALIKE**
Project Name	:	Executive Engineer Project Division
Consultants	:	Improvements, Restoration to roads and drains at Dasarahalli, Saraipalya and Rachenahalli surrounding areas in ward no.06
Project Manager /Team Leader	:	Civil Pro
Project Start Date	:	Karthik Rechan
Project End Date	:	01-07-22
Project Length in Months	:	07-04-23
	:	09 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
12	KSRRB M400-17. Providing, laying, spreading and compacting cushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers with paver in	Sqm	21662.92	21662.92	100	08-08-22	02-10-22	55
13	KSRRB M500-6. Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM including cleaning of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means complete as per	Cum	64272.97	64272.97	100	18-08-22	17-09-22	30
14	KSRRB 500-2. Cleaning the existing black topped surface with brooms, soft brushes and finally dusting with old gunny bags and / or compressed air to receive bituminous treatment including cost of all materials, labour, HOM complete as per specifications. (P.No-158,I No-21.2,KPWD SR 2018-19)	Each	6066.86	6066.86	100	07-09-22	06-12-22	90
15	KSRRB 500-7. Providing and applying tack coat using 80/100 grade bitumen(VG10) on the prepared black topped surfaces at 2.5 kg per 10 sqm, heating bitumen in boiler fitted with spray set (excluding cleaning of road surface) including cost of all	Each	38811.65	38811.65	100	17-09-22	16-12-22	90
16	KSRRB M500-17. Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade, level and	Cum	279.61	279.61	100	18-08-22	17-09-22	30
17	Providing and laying bituminous concrete 40mm thick with hot mix plant, using crushed aggregates of specified grading, premixed with bituminous binder and filler, transporting the hot mix to work site, laying with a paver finisher to the required	Cum	3906.08	3906.08	100	17-09-22	16-12-22	90
18	KSRRB M800-13.Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface/ Concrete Surface: Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising	Cum	3185.4	3185.4	100	07-10-22	26-12-22	80
19	KSRRB M200-24. Dismantling of cement concrete pavement by mechanical means using pneumatic tools, breaking to pieces not exceeding 0.02 cum in volume and stock piling at designated locations and disposal of dismantled materials upto a lead of 1000	Sqm	1076.12	1076.12	100	03-08-22	22-09-22	50
20	KSRRB M600-1.Providing and Constructing dry lean cement concrete mix CC 1:5:10 base with OPC 25mm and down size graded granite metal coarse aggregate at 0.86cum and fine aggregates @0.58cum over a prepared sub-base, coarse and fine aggregate conforming to IS: 383-2016,aggregate cement ratio not to exceed 15:1, Aggregate gradation after blending to be as per	Sqm	645.99	645.99	100	13-08-22	12-10-22	60

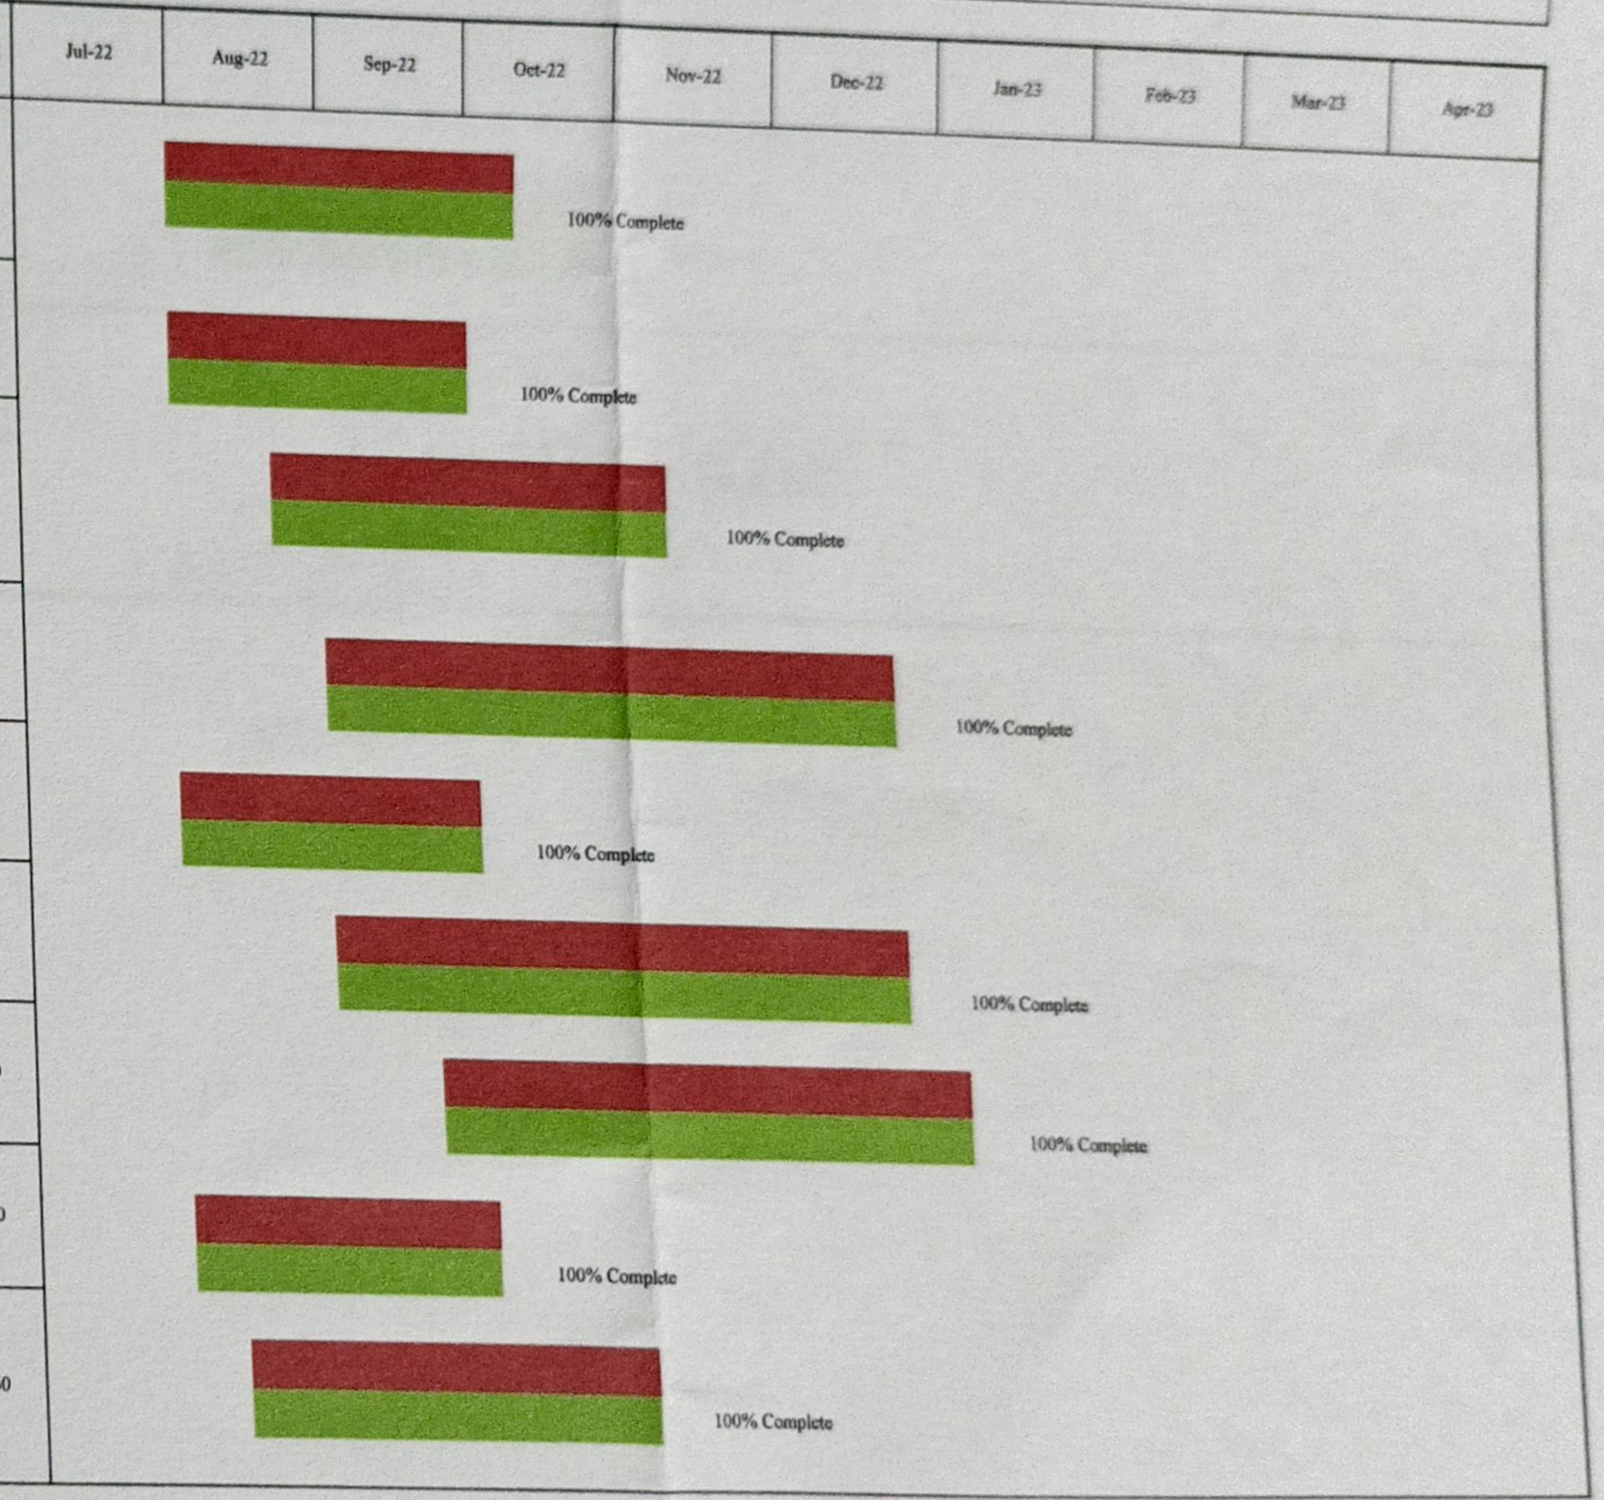

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

BRUHAT BENGALURU MAHANAGARA PALIKE

Client Name	:	Executive Engineer Project Division
Project Name	:	Improvements, Restoration to roads and drains at Dasarahalli, Saraipalya and Rachenahalli surrounding areas in ward no.06
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	01-07-22
Project End Date	:	07-04-23
Project Length in Months	:	09 Months

Sl. No	Assignment	Unit	Modified Schedule Qty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23
21	Constructing un-reinforced, plain cement concrete for pavements using Grade concrete M30 with OPC at 360 kg/cum and coarse aggregate 0.69cum, fine aggregate 0.46cum. over a prepared base with OPC coarse aggregate at 0.69 cum, fine aggregates at 0.46 cum,Coarse and fine aggregate conforming to IS:383-2016, with Superplastizer at 3 lts conforming to IS 9103-2008. mixed in a	Cum	645.99	645.99	100	23-08-22	27-10-22	65					100% Complete					

= Planned %

= Executed %

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner
